
TNi PROJECT MANAGER | PROJECT DELIVERY FLOW

PROCESS BOX = ACTION + DELIVERABLE / DIAMOND = DECISION / YES / NO = BRANCH / LETTER CIRCLE = CONTINUATION


LEVEL A - DEFINE & RELEASE

OBJECTIVE: Establish scope, budget, schedule and authorized purchases.

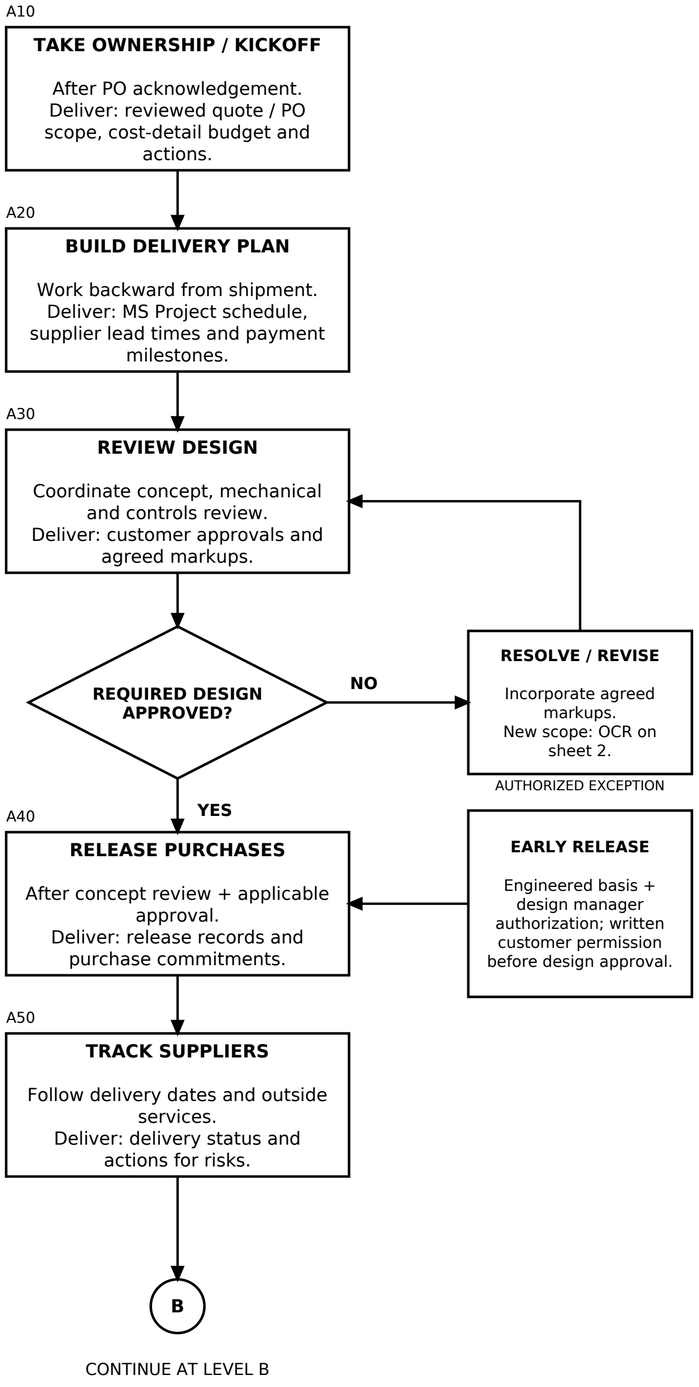


LEVEL B - BUILD, PROVE & SHIP

OBJECTIVE: Demonstrate requirements and release equipment for shipment.

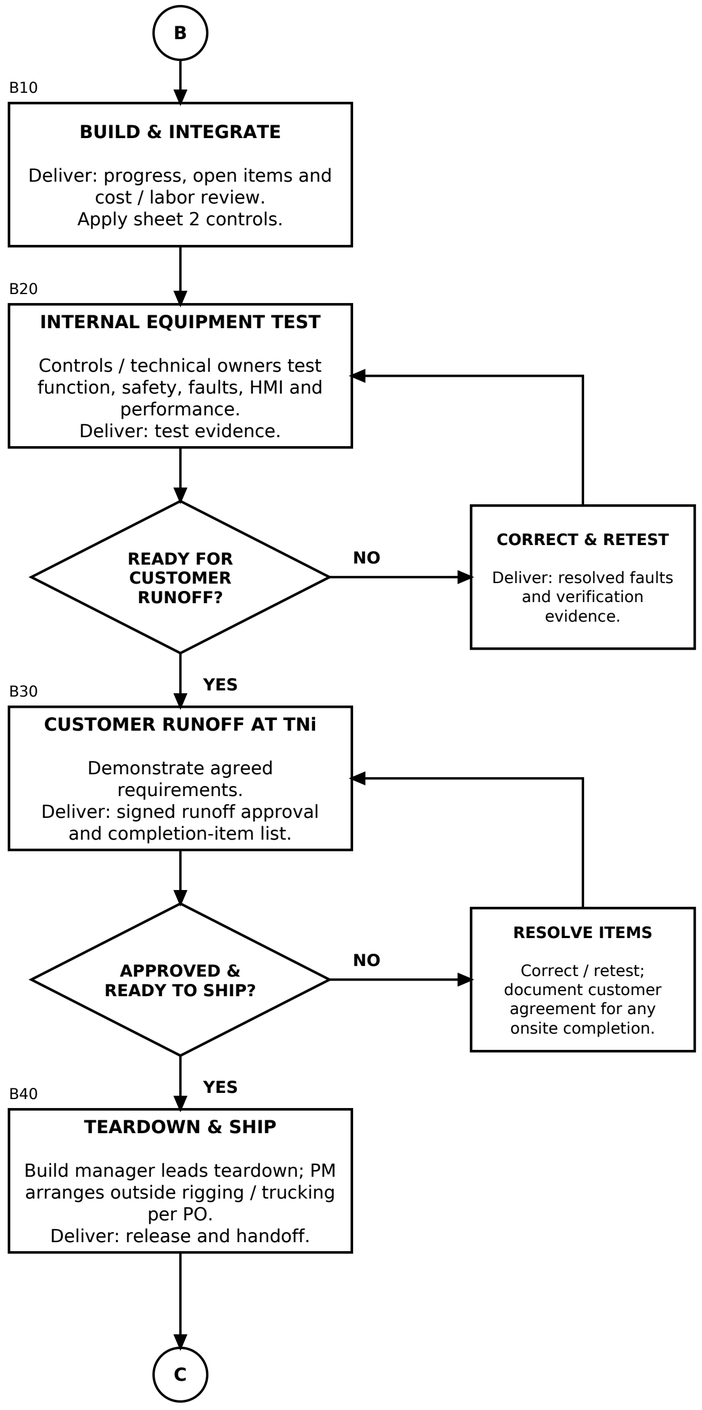

LEVEL C - ACCEPT & CLOSE

OBJECTIVE: Prove performance onsite, complete obligations and support warranty.

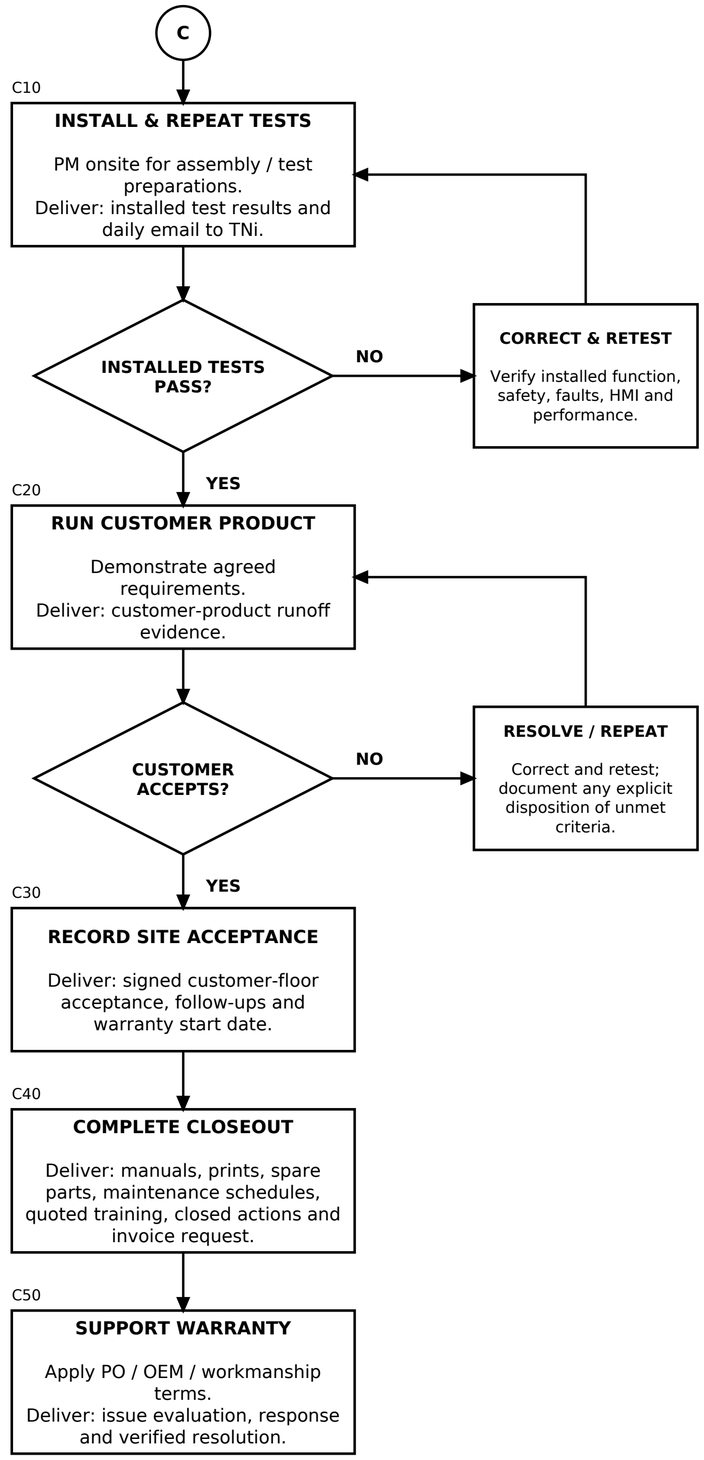

TNi RUNOFF APPROVAL IS DISTINCT FROM FINAL CUSTOMER-FLOOR ACCEPTANCE. UNRESOLVED SAFETY FAULTS STOP AFFECTED TESTING.

TNi PROJECT MANAGER | CONTINUOUS CONTROLS & EXCEPTIONS

PROCESS BOX = ACTION + DELIVERABLE / DIAMOND = DECISION / YES / NO = BRANCH / LETTER CIRCLE = CONTINUATION

CONTROL 1 - SCOPE CHANGE

OBJECTIVE: Authorize added work and preserve separate OCR accounting.

X10

CUSTOMER REQUEST

Compare request with agreed quote / PO scope.

OUTSIDE AGREED SCOPE?

NO

EXISTING JOB

Manage within scope. Internal overrun alone does not establish OCR.

YES

X20

PREPARE OCR QUOTE

Engineering defines added work and cost / schedule effects.
Deliver: TNi OCR quotation.

WRITTEN CUSTOMER AGREEMENT?

NO

PENDING

Clarify / revise quote. Do not begin added work without agreement.

YES

X30

AUTHORIZE OCR WORK

Written agreement generally permits proceeding; pursue separate customer PO.
Deliver: agreement and PO.

X40

SEPARATE JOB / ACCOUNTING

Preserve original budget. Revise dates only for actual added days.
Deliver: OCR job and revised plan.

RETURN TO AFFECTED PROJECT ACTIVITY

CONTROL 2 - DELIVERY RISK

OBJECTIVE: Recover threatened milestones and control revised commitments.

R10

IDENTIFY DELIVERY RISK

Supplier, department or customer delay.
Deliver: affected work and milestone assessment.

R20

ESCALATE TO OPERATIONS

Develop recovery with affected department.
Deliver: recovery actions and owners.

RECOVERY PROTECTS SHIPMENT?

YES

EXECUTE RECOVERY

Track actions and update schedule.

NO

R30

AGREE REVISED DATE

Operations reviews with general manager.
Deliver: internally agreed shipment date.

R40

COMMUNICATE & UPDATE

PM communicates agreed date to customer.
Deliver: revised schedule and open items.

R50

MONITOR TO RESOLUTION

Discuss actual customer-caused impact; no automatic day-for-day extension.
Deliver: action closure.

URGENT THREATS: DO NOT WAIT FOR THE WEEKLY PRODUCTION MEETING.

CONTROL 3 - PM REPORTING

OBJECTIVE: Keep the customer and TNi informed throughout execution.

P10

WEEKLY CUSTOMER REPORTS

Schedule PDF from MS Project + Excel open-items PDF showing TNi and customer items, owners and status.

P20

CUSTOMER MEETING

Meet weekly or biweekly.
Deliver: decisions, new actions and recorded customer impacts.

P30

WEEKLY PRODUCTION MEETING

Present schedule adherence, roadblocks and required management intervention.

P40

WEEKLY SAGE REVIEW

Review actuals, hours, open POs, commitments and remaining work; avoid double counting.

BUDGET CONCERN?

Address recognized concerns directly with general manager.

P50

ONSITE DAILY UPDATE

Record events / completion throughout customer-site build; email TNi at end of day.

P60

PAYMENT MILESTONE

PM initiates invoicing when earned.
Deliver: milestone / final invoice request; accountant executes.

CADENCE CHECKLIST: REPEAT AS APPLICABLE; THESE ARE NOT RELEASE GATES.

BASIS: TNi PM Academy v1.2; equipment runoff checklist Draft 02; agreed TNi process clarifications. PM coordinates and verifies; qualified technical owners perform technical work.
